




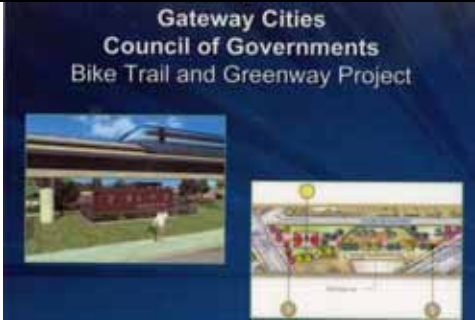











ACTIVE PROJECTS FUNDED BY THE RMC, Status as of July 7, 2006 (Sorted by Project Name)




Photo	Project Name	Applicant	RMC No.	Project Description	Project Status	Project Category	Acquisition (Acres)	Funding
	Alhambra Wash Naturalization	Amigos de los Rios	3264	Preparation of an initial feasibility assessment for naturalization of Alhambra Wash. The study will analyze historic conditions and current flows to evaluate the feasibility of recreation and habitat improvements along the segment of the wash between Walnut Grove and the Rio Hondo.	Comments on the draft report have been submitted.	Planning	0	\$40,750
	Anaheim Coves/ Burris Pit Park Development	City of Anaheim	3576	The Burris Pit/Anaheim Coves project is the development of a trail with landscaping and interpretive elements around a recharging pond in the City of Anaheim. It is a collaborative project between the City and the Water District. The City of Anaheim and the Orange County Water District (OCWD) have entered into a partnership, allowing the City to develop recreational uses at the site of one of the District's ground water recharge basins, known as the Burris Pit. The first phase of work will largely consist of refurbishment of existing landscaping with native vegetation and irrigation, parking for 12 cars, asphaltting and fencing the road, fencing to separate public use areas from the water, picnic tables, benches, barbecues, interpretation signage and entry improvements.	The City has completed the lease agreement with the water district. A design team has been selected and the environmental work is ahead of schedule.	Planning + Development	0	\$841,610
	Arcadia Wash Restoration Feasibility Study	Amigos de los Rios	3268	Assessment of feasibility for removing approximately 2,400 linear feet of concrete lining in the Arcadia Wash, including hydrologic assessment, geomorphologic study, assessment of golf course impacts, and hydraulic design.	Grantee revisions include adding information on the Racetrack portion of the project based on the latest proposal of Caruso for the Santa Anita Shops. These edits and additional information will be submitted to stakeholders for comments. Once comments have been received from stakeholders the final draft will be submitted to RMC in June.	Planning	0	\$152,523





	Azusa River Wilderness Park Acquisition	Watershed Conservation Authority	3260	The Azusa River Wilderness Park is a project to create a passive park on the north end of the City of Azusa at the beginning of San Gabriel Canyon. The envisioned park is 89 acres in size with acreage on both sides of the San Gabriel River. There are opportunities to work with a variety of agencies and to connect to several trails that travel into the Angeles Forest as well as the San Gabriel River Bike Path that travels the length of the river and whose terminus is in Seal Beach.	The Taylor parcel has been purchased by the City of Azusa and the El Encanto site has been acquired by the WCA. Ranger Services are being provided by the Mountains Recreation and Conservation Authority who are patrolling and doing minor upkeep of the park. The minor refurbishments are in the design and permitting process. The WCA has awarded a contract for Planning & Design of the Park to Blue Green Consulting with the planning beginning in June.	Acquisition (+ Planning + Development)	39.9	\$1,284,920
	Azusa River Wilderness Park Planning and Implementation - Prop 40	Watershed Conservation Authority	3596	Planning and Implementation for the Azusa River Wilderness Park. This process will produce a plan for the Azusa River Wilderness Park with specific Plans for the El Encanto property.	The Grant documents are in process of execution and the Design Team is on board and beginning work.	Planning	0	\$875,945
	Bellflower Riverview Park	City of Bellflower	3238	This project will create a recreation area fronting the San Gabriel River. The project will provide a natural, riverfront environment serving not just the residents of Bellflower, but numerous communities located up and down river. Proposed improvements include a paved bikeway, landscaping, park benches, lighting, and informational signing. A direct link to the San Gabriel River bikeway will be created, as well as linkage to the City of Bellflower West Branch Bikeway currently in the preliminary engineering phase of development. Funds not used for acquisition were redirected from 3261.	Acquisition of the tax-default parcel was completed 12/28/05. Conceptual Plans have been reviewed by the City Council and the RMC. These were submitted to SCE for review and comment, and revised plans based on SCE comments are now back at SCE for review. Once SCE approves the conceptual plans, they will be forwarded to PUC for approval, then SCE and the City can enter into a sub-lease for the 11 acres, ensuring land tenure. Amendment 3 has been processed to update the budget and timeline, and to include redirection of \$200K from RMC 3261, as City has purchased 3.9 acres of property for the Park. This extension was approved by the RMC Board on 3/20/06.	Planning + Development	0	\$300,000
	Bikeway Plan-Gateway Cities	Gateway Cities Council of Governments	3252	This plan will coordinate, prioritize and comprehensively evaluate the regional bikeway needs in the Gateway Cities area. Conceptual plans are underway and negotiations with public agencies related to right of way development components continue.	To date the Steering Committee has reviewed consultant approach and toured project in Paramount. Cities are beginning review of possible RMC objectives along the pathway. Field review, review of applicable plans, policies and documents are 50% complete. Aerial survey has been conducted and base map preparation is in progress. Discussions were also in progress with MTA as to allowable uses of property. Amendment of scope of work and timeline are needed.	Planning	0	\$250,000




	Brownfield Study-San Gabriel Valley	San Gabriel Valley Council of Governments	3251	Brownfields in the San Gabriel Valley COG area were identified for possible open space and economic development opportunities. Currently, ranking of the sites for future development as open space uses is underway and the project should be complete in Fall 2006. Approximately \$65,000 funding will be returned to the RMC due to a smaller scope of work than originally anticipated.	Inventory of Brownfield sites is complete but yielded a smaller number of sites than anticipated. Staff is working with the grantee to identify the most beneficial adjustment to the scope of the remaining work. No further work has been completed since the previous report. A grant amendment for classification and extension of performance end date will be processed.	Planning	0	\$250,000
Project Management	Capital Project Management Services	Mountains Recreation and Conservation Authority	3601	At the direction of the San Gabriel and Lower Los Angeles Rivers and Mountains Conservancy (RMC) Executive Officer, the MRCA shall perform project management tasks for projects on the RMC Workprogram.	Services provided under this grant included project management for RMC workprogram grants. Project Management services included development of project concepts with applicants, negotiations regarding the scope of work and budget, administration of grant agreement and close out of projects.	Multiple Category	0	\$353,538
Project Management	City of Long Beach Project Management Services	City of Long Beach	3593	The Long Beach Project Services Management grant is to the City of Long Beach Real Estate Division for services on acquisition.	5/18/06 the grant has been redirected from WCA 320004 to this RMC grant. The executed grant was sent to the State for certification on 5/17/06.	Multiple Category	0	\$100,000
No Photo	Compton Creek	Los Angeles and San Gabriel Rivers Watershed Council	3599	The grant will provide funding to LASGRWC for implementation of the Compton Creek Watershed Management Plan and to build local capacity to plan for, manage, and construct watershed projects within the plan territory.	RMC Board approved a grant of \$50,000 to fund ongoing implementation strategies for the watershed plan	Planning + Development	0	\$50,000
	Compton Creek Regional Garden Park	City of Compton	3246	The project is a multi-use recreational facility consisting of 3.3 miles of trails along Compton Creek connecting nearby parks, nature classrooms, and nature preserves within the watershed. The project includes bike paths, walking, jogging and hiking trails, equestrian trails, a native plant arboretum, nature classrooms, tree planting and security.	A draft report has been prepared and comments have been submitted to the consultants.	Planning	0	\$100,000
	Coyote and Carbon Creeks Watershed Management Plan	County of Orange	3213	This project is to develop a watershed plan for the Coyote and Carbon Creek Watershed, a tributary of the San Gabriel River, in order to maintain, restore and enhance a healthy 155 square mile watershed.	Two of the technical memos are at 90% completion, Existing Conditions & Opportunities and Constraints. The series of existing conditions maps is nearly complete. Participation in the bi-monthly workshops has been strong 30-40 City, nonprofit & agency representatives. The project is on track to be completed in January '07.	Planning	0	\$150,000


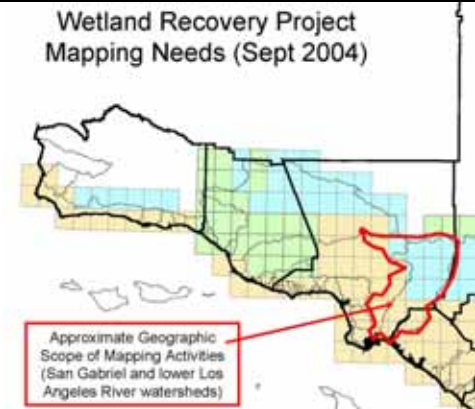

	Coyote Creek Bike Trail Connection to Cerritos Regional Park	City of Cerritos	3584	The Coyote Creek Bike Trail Connection to Cerritos Regional Park is a project that will enhance the two accesses to the Coyote Creek Bike Path. RMC staff has been working successfully with the City of Cerritos in defining the gateway/access area to Coyote Creek. The improvements include an improved gateway at Shoemaker Street, a pedestrian ramp for ADA access, and trail identification signage. There would be new fencing from the improved gateway on Shoemaker to the City's maintenance building.	The City is nearing completion of the design process and is moving forward with its permits with LA County Flood Control District.	Planning + Development	0	\$250,000
	Coyote Creek Regional Trail System Improvements	Trails 4 All	3580	The Coyote Creek Regional Trail System project is an assessment of the Coyote Creek Bike Trail as well as signage and some greening projects.	There have been three planning committee meetings with representation from many of the cities, agencies, business and organizations along Coyote Creek. There have been three field trips to do a ground truthing assessment of the trail. The mapping is proceeding and is at about 70%. The agreement to share GIS data from the County of Orange is in place. The planning has begun for the Bike fairs in the parks that will precede the community stakeholders workshops.	Planning + Development	0	\$250,000
	Coyote Creek-Los Alamitos Improvement Project	City of Los Alamitos	3318	The Coyote Creek-Los Alamitos Improvement project is the creation of a park out of an underused space along Coyote Creek. This project will also add to other improvements along Coyote Creek with the ultimate goal of greening this tributary of the San Gabriel River.	. The City has been working with the RMC staff and SCE staff, negotiations produced a short term lease. The parties are working together to go forward to the PUC to negotiate a long term lease. The City has hired Withers and Sangren to develop the design of the park, concept designs completed and being reviewed.	Planning + Development	0	\$1,440,000




	Dominguez Gap Wetlands Restoration Multi-use Project	County of Los Angeles Department of Public Works	3232	The Dominguez Gap Wetlands Multiuse project proposes to modify two existing retention basins located on each side of the Los Angeles River to create 12 acres of functional wetland and riparian habitat, improve water quality and recharge, create passive recreational facilities, including trails, shade structures, and interpretive signage, along with providing educational features, and improve aesthetic values. Furthermore, this project provides direct access to the 51-mile Los Angeles River Parkway. Funding for construction is not recommended at this stage since the project is still in the planning phase. In fact, the Deforest Park project and this project may be combined to make more efficient use of funds that may be provided by the Coastal Conservancy.	Plans are at 100% completion and work has begun on design of interpretive signage for the Project. Bids are expected to be received on May 23, 2003. Notice to proceed will be issued once contractual details are resolved.	Planning + Development	0	\$200,000
	Dominguez Gap/De Forest Park Restoration	Los Angeles County Flood Control District	3583	This project provides for several options: 1- Extend wetlands in the northern .5-mile of the basin and restore marsh and low riparian habitat. Construct small interpretive center, improve walkways, and add interpretive signage. Selectively remove exotic trees and shrubs and replace with high riparian woodland trees. Restore southern .75-mile as native scrub and riparian habitats. CH2M hill feasibility study completed June 2002. (\$2.2 million); 2: Option 1 with enhanced water supply from the LA River (\$6.3 million); 3: Revise grading of site to flow from north to south for the entire length of the basin for wetlands and diverse habitats. Enhance water supply from LA River or CalTrans 105 Source.	This project is still pending an agreement between Los Angeles County Flood control District. and the City of Long Beach. An application for funding under the River Parkway Grant Program is currently being reviewed by the Resources Agency	Planning	0	\$100,000
	Duck Farm Geotechnical Studies	Mountains Recreation and Conservation Authority	3273	The grant provides for geotechnical sampling on the Woodland Duck Farm property and independent analysis of the sampling results. The primary deliverable, a geotechnical report on the porosity of the underground strata will determine the feasibility of groundwater recharge at the site.	The final results of testing have been reviewed by the Los Angeles County Department of Public Works. The report indicates that the area tested is not suitable for groundwater recharge. These findings will be used by the site master plan consultant team.	Planning	0	\$146,756




	Duck Farm Planning	Watershed Conservation Authority	3243	The purpose of this project is to create a Master Plan for the Woodland Duck Farm property. The products of the Phase 1 planning will be community outreach and visioning, data gathering and analysis, feasibility Studies for access, circulation, watershed improvement projects etc., identification of feasibility analysis needs, commencement of an Interim Public Use Plan, and recommendation for funding strategies and opportunities. The plan will incorporate a finding under CEQA.	The first phase of the planning is almost complete. Input from stakeholders has been gathered and is currently being analyzed for use in the development of design alternatives. The review of concept alternatives is underway and input from stakeholder is being sought. A public meeting to review the draft alternatives is planned for July 15, 2006 at San Angelo Park.	Planning	0	\$330,000
	Duck Farm Traffic Studies	Mountains Recreation and Conservation Authority	3274	The grant provides for CEQA documentation; a traffic study on the Woodland Duck Farm property and for professional services related to the project. The CEQA documentation is required under state law for the project. The traffic study will assist in determining the limitations on public access and establish threshold for limited access by RMC and WCA staff. The grant also funds legal services associated with review of easements on the property.	This grant has been redirected to planning and/or improvements for the project.	Planning	0	\$45,331
	East Los Angeles Civic Center Improvements	County of Los Angeles	3259	Assist in creating a sustainable, educational water feature connecting the plaza through open space	The Board of Supervisors has approved the budget for this project. Final design of the fountain is pending approvals by the Health Dept. and other permitting agencies.	Planning + Development	0	\$500,000




	El Dorado Regional Park Wetlands Feasibility Study	City of Long Beach	3208	The City of Long Beach will study the feasibility of bringing the urban run-off flow of the San Gabriel River through El Dorado Regional Park, Nature Center, and proposed Wetlands to make the park's lake and stream systems part of the San Gabriel River System in a 2.3-mile long riparian habitat. The partially developed northwest corner of the Regional Park would be developed as wetland to help remove pollutants, and natural riparian habitat would be restored along the stream. Picnics and events would be scaled back to prevent undue disturbance,	The initial feasibility study is complete and the City staff has reviewed and commented on the draft. The final report is completed and the final minor edits are being completed prior to the printing of the final report and presentation to the RMC.	Planning	0	\$100,000
	Ferguson and Wildwood Pre-Acquisition Expenses	City of Glendora	3566	The Ferguson and Wildwood properties are two large, diverse open spaces in the foothills of the San Gabriel Mountains. This grant will pay for the appraisals and appraisal reviews enabling the City of Glendora and the City of San Dimas to seek funding for acquisition.	The appraisals of Ferguson and Wildwood Canyons are complete. The state review of the appraisals for Wildwood and Ferguson are complete and supported. The work for this grant is now completed, with the request for payment and a final report the final tasks to be completed.	Acquisition (+ Planning + Development)	0	\$50,000
	Galster Park Project	City of West Covina	3229	Amendment of 5/16/05 changed scope of work. Funds previously earmarked for improvements to the hill top Boys Camp (\$150,000) to be relocated to the family camp, making it a fully functional ADA accessible campground. The trails, restrooms, and signage will be upgraded. Landscaping will also be enhanced with native plants. Plans are 100% and bidding to select a contractor is underway.	As of April 2006, construction is underway. The RMC approved modifications to the work plan and the project is expected to be completed on schedule.	Planning + Development	0	\$476,000
	Gibson Park Habitat Plantings	City of El Monte and Amigos de los Rios	3337	Part of the Emerald Necklace, Gibson Park grant from the RMC will fund native landscaping, an outdoor interpretive kiosk and an outdoor classroom where visitors and school children can learn about the natural history and resources of this area of the watershed.	Amigos continues with to work on development of construction drawings for the Park.	Planning + Development	0	\$433,500




	Gordon-Mull	City of Glendora	3223	Gordon-Mull is a 42 acre acquisition which provides for the protection and enhancement of two blue-line streams and connected wetlands, sensitive plant communities. A hiking trail is proposed, a small house will be refurbished as a nature center and a habitat/restoration plan would be prepared and implemented with Glendora Community Conservancy.	The appraisal and the state review of the appraisal are complete. The plans for the alternative waterline have been reviewed by the City and RMC staff. The City Dept. of Public Works is working with the owner's engineer to design the waterline and easements for the waterline realignment.	Acquisition (+ Planning + Development)	42	\$2,500,000
	Graham Elementary School Watershed Education Trail Phase II	North East Trees	3340	This grant will fund improvements to an existing alley used to access Graham Elementary by parents and school children. Funded elements include landscaping and interpretative signage as well as an environmental art project to be conducted by the children of Graham elementary.	NET has submitted applications for permits and is waiting for approval before proceeding.	Planning + Development	0	\$50,920
	Green Visions- Habitat, Trail and Recreational Access Plan	Watershed Conservation Authority	3240	The product of this grant is a framework for the Green Visions Plan. The deliverables included a plan inventory, online plan library and map, data scan and analytical framework and workshop.	Grantee has completed Phase I and received an extension on the Bridge Funding Phase. They have released the both a Target Species Report and Recreational Assessment planning reports. Work on the development of GIS and related tools is on-going.	Multiple Category	0	\$500,000
	Green Visions Phase II	Watershed Conservation Authority	3568	This Phase II project is to implement the major tasks identified in the Phase I framework, to identify and assess opportunities for habitat conservation and restoration, open space acquisition and recreational facilities development, and watershed protection efforts. The GIS planning tool and data sets will also be created. To retain its utility, the data infrastructure associated with this tool will need to be managed. This phase of the project will span at least two years, with a start date of January 1, 2005.	This grant provides funding for Phase II of Green Visions which will include the development and release of specific GIS tools related to target species, park and open space data, hydrological modeling information, and other essential planning tools.	Multiple Category	0	\$500,000





	Habitat Authority Community Outreach & Education	California Native Habitat Endowment Fund	3233	This project is to put together a curriculum to train the trail and program volunteers (Docents) on the Puente Hills Landfill Native Habitat Authority properties.	This grant has been redirected to the Puente Hills Habitat Authority which now has the staff to facilitate the work to be completed.	Interpretation	0	\$20,000
<p>Wetland Recovery Project Mapping Needs (Sept 2004)</p>  <p>Approximate Geographic Scope of Mapping Activities (San Gabriel and lower Los Angeles River watersheds)</p>	Historical Ecology of the RMC Territory	Southern California Coastal Water Research Project	3556	This project will: 1) Define and prioritize historical research questions to meet restoration and management information needs; 2) Develop historical data archive and database; 3) Develop initial land use history map and timeline; 4) Digitize and georectify key historical data sets; and 5) Assess the relative value of different historical data sources to answer pressing environmental management questions.	The project team met over the last quarter and refined the scope of work for the project based on the overall stated project goals. The revised work plan includes a refinement of the spatial and temporal scope of the analysis that will ensure we complete the project by December 2006. The revised plan was submitted to the RMC for review and comment. The project team met with the Habitat and Science Advisory Panel (HSAP) in January 2006 to review the revised scope of work. During the 1st Qtr 2006, the project team completed elements of the first four project tasks. In January 2006, the team met with the Habitat and Science Advisory Panel (HSAP) to discuss the overall scope and approach to the project. The HSAP generally agreed with and supported the direction of the project team. Throughout the past quarter, the team has compiled extensive maps on the topography, land use, soils, and geology of the watershed. Over the next quarter, the project team will meet with the Stakeholder Group (on May 3, 2006)	Planning	0	\$148,000
	Invasive Weed Control in Riparian Habitat of San Gabriel Valley	Los Angeles and San Gabriel Rivers Watershed Council	3359	Undesirable invasive non-native plants will be selectively controlled by targeted herbicide applications, requiring minimal cutting and biomass reduction, performed by Riparian Repairs, a licensed pest control business, as subcontractor to the Watershed Council, extending and expanding previous habitat restoration work initiated during the year 2000 to: Rio Hondo Riparian Corridor, San Gabriel. River channel at Whittier Narrows, Whittier Narrows Nature Center, Santa Fe Dam Basin and San Gabriel. River channel in Azusa, and Eaton Canyon Nature Center.	Inspection and reapplication of herbicide is ongoing as part of the eradication process.	Planning + Development	0	\$36,000




	La Mirada Creek Restoration Planning	City of La Mirada	3225	The project would plan for 1): The removal of numerous sick and dying trees, replanting of native species, leveling of turf along trail at Oak Creek Park, revegetation of additional areas, rebuild of amphitheater at Creek Park, and interpretive signage regarding the wildlife and native vegetation in the area. 2) :Replacement of two bridges damaged by previous storms, repair horse trail paths and plant native vegetation along the sides, reslope the path to the public restroom facilities (ADA), and install three stormceptor devices along La Mirada Creek to keep pollutants for entering the stream.	An agreement between Los Angeles County Department of Public Works and the City of La Mirada to conduct the planning is pending. Planning will proceed once the agreement is signed.	Planning	0	\$150,000
	La Verne Open Space ANF Connection (Project 1)	La Verne Land Conservancy	3367	The La Verne Open Space project is an enhancement of open space being purchased by the City of La Verne in the Marshall Canyon Area of the San Gabriel Foothills. The La Verne Land Conservancy will operate and maintain the property. There will be trailhead signage, improvements and interpretation to the local students and community groups.	The LVLC has engaged a consultant and has begun the planning process with two stakeholders meetings. The Conservancy & the Mia Lehrer have begun the preliminary designs and is looking into drainage issues on the properties.	Planning + Development	0	\$208,000
	Laguna Lake Park Master Plan	City of Fullerton	3222	The Laguna Lake project in the City of Fullerton is a restoration of a park designed and utilized since the 1950's. The Coastal Conservancy and the RMC are working on reviving the fishing lake, the pathways and landscaping along the lakeside. The renovation will include a new parking lot, outdoor classroom, restroom, picnic areas, fishing piers, ADA accessible walks and ramps, realignment and regarding of park trails, addition of retaining walls and new landscaping and irrigation. The RMC Grant will support a combination of grants and fund the master plan, refurbishment of the trail and landscaping on one side of the lake.	The lake has been refurbished with a new filtration system and is currently being stocked by Dept. of Fish & Game. The master plan is completed, with City and RMC staff prioritizing the phases and beginning refurbishment of the trail and landscape in the next quarter.	Planning + Development	0	\$500,000




 <p>Barren stream bank Arundo donax patch Castor bean patch Reduced flow capacity</p> <p>Exotic Vegetation, Erosion and Debris Issues</p>	Lario Creek Enhancement Project	County of Los Angeles Department of Public Works	3231	This grant will provide planning funds for stream bank stabilization and restoration while increasing the channel's ability to divert water for groundwater replenishment. Stream bank stabilization and restoration will be accomplished using bioengineering techniques, removing invasive vegetation, and revegetating with native plants. Enhancing and restoring the vegetation will also promote ecological diversity, provide additional wildlife habitat, and increase its educational value. The resulting project will contribute significantly to the recreational opportunities for the communities of South El Monte, Pico Rivera, Whittier, and other nearby communities. The site is proposed to be open to the public to enjoy the low impact recreational amenities and educational opportunities.	The planning consultant has developed two concept alternatives for the realignment of Lario Creek. Review of the two alternatives by Los Angeles County Department of Public Works is still in progress.		0	\$125,000
	Lashbrook Park	City of El Monte	3372	Lashbrook Park is a creation of a park out of unused land along the Rio Hondo River. The land is owned by the US Army Corps of Engineers. Lashbrook Park will be developed into a neighborhood park and rest stop for the bike trail on the Rio Hondo River. The existing vacant property will be landscaped with trees and turf, new fencing, security lighting, and picnic benches. A grant was applied for through the LA County Regional Park and Open Space Bond Act. The RMC funded portion is for native landscaping in staff expertise.	The bio swale zone has been completed, the trail construction is complete along with the watering system and some plantings. The park is complete and was opened on January 28th, 2006.	Planning + Development	0	\$71,000
	Legg Lake Fishing Pier	County of Los Angeles Department of Parks and Recreation	3373	This grant will provide restoration of an area of North Legg Lake by implementing a shoreline restoration program which includes ADA parking, an access walkway and ramp, an informational kiosk and native landscaping.	The RMC & County Parks have processed a second amendment to the grant. The Dept of Fish & Game is requiring an updated biological survey, which will take up to 8 weeks. The new project end date will be June 30, 2007. 90% construction review plans (NIC landscaping), the biological survey and technical specifications were received by RMC on 3/23/06.	Planning + Development	0	\$500,000



	Lemon Creek	City of Walnut	3374	There are flood improvements and clearance of the creek area that need to be completed, past flood control measures have uprooted concrete preventing the natural flow of the creek.	a contractor has been selected and demolition work has begun.	Planning + Development	0	\$225,000
	Long Beach Aquarium Watershed Exhibit Expansion Project	Aquarium of the Pacific	3570	This grant facilitates the completion of the "Long Beach Aquarium Expansion Project - RMC 3257" for design and planning. The project includes construction and installation of a LEED certified classroom, native landscaping, a public exhibit at Pier Point Landing and a watershed exhibit consisting of watershed tables and interactive interpretive displays. The "green" classroom, which will be certified at LEED Platinum level. The project is moving forward, with the exception of the green classroom construction. The City of Long Beach has requested assistance of Congresswoman Millender-McDonald for quick resolution with the National Park Service regarding the land exchange to facilitate the location of the classroom. Selection of a contractor and groundbreaking originally planned for August 2006 have been delayed.	Project is on hold pending resolution of land tenure with the Federal Government. The Long Beach Aquarium expansion project is a creation of a classroom and interpretive exhibits that are focused on the San Gabriel and Los Angeles River Watersheds. The Aquarium has ongoing fundraising and grant applications for further funding due to construction cost increases. The Aquarium has joined the City of Long Beach's Green Building Team to help implement green building policies. The permit process and land swap with the City of Long Beach is moving forward. The exhibit planning is moving forward in the next quarter with a stakeholders meeting, utilizing the new exhibit designer on the Aquarium's staff. Contractor proposals are under review Spring 2006.	Planning + Development	0	\$1,322,000
	Los Angeles River Bike-way Path Enhancement and Rehabilitation	City of Bell	3380	Enhancement and rehabilitation of the bikeway path to include removal of dilapidated chain link/barbed wire fence, installation of native California vegetation, drip irrigation, decorative wrought iron fencing and river rock. The City has contracted LA DPW Watershed Department to conduct all work. 100% plans have been generated and the project is expected to be complete by late 2006. Funds from LA Watershed and Resources Agency are also being used to develop adjoining sections of the bike trail with the same design components, running through Bell and into City of Cudahy.	Kick off for the construction was held at the April Earth Day event for the Los Angeles River. The City of Bell will be improving the path from Gage to Fostoria Street along the Los Angeles River in the City. The RMC funds provide native plantings, irrigation and river rock hardscape between Gage and Florence. LA County Watershed is the subcontractor for both Bell and Cudahy. 100% plans were provided to RMC for review on 2/1/06. RMC has revised timeline, but end date, scope of work and budget remain same, so no amendment necessary.	Planning + Development	0	\$200,000



	Lynwood Meadows	City of Lynwood	3226	Lynwood Meadows project will rehabilitate a vacant city-owned property as a park. The project is located in a densely populated community. The majority of the park is proposed to be open space, with a shaded picnic area, a tot lot and basketball courts. Alternate funding has been identified for non-passive components. The City will utilize native vegetation and open space components in compliance with RMC requirements.	The grantee is in the process of completing the design plans. A comprehensive Workplan is in place for the development of the park. A time extension has been processed for this project.	Planning + Development	0	\$562,379
	Maywood Bikeway Access	North East Trees	3394	Funding will provide for an enhanced and naturalized bikeway access with native planting, permeable surface, bench seating, and other amenities on the north side of Slauson Avenue at the LA River. The project is identified in the <i>Los Angeles River Bikeway and Greenway Planning Study</i> .	Development and review of concepts for this project is ongoing. NET is working with the City of Maywood to coordinate the Bikeway improvements with street improvements by the City. The next round of design review is scheduled for the coming weeks	Planning + Development	0	\$208,254
	Maywood Riverfront Park	City of Maywood	3395	The project has taken abandoned industrial and Superfund sites and converted them into a riverfront park with connections to the LA River Bike Trail. RMC board approved \$250K to complete construction	Grant agreement has been executed and work has begun on the project. Expected completion date is June 30, 2006.	Planning + Development	0	\$250,000



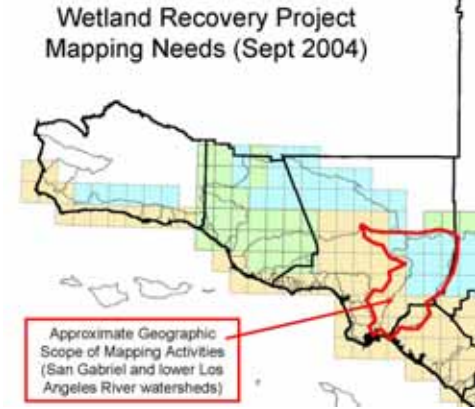
	Mines Avenue Bike Lane Improvement Project	City of Pico Rivera	3269	Bike lane enhancements including re-surfacing the bike lanes, curb and gutter reconstruction, striping and signage.	The final design plans were reviewed by the RMC and are being submitted to the City Council for approval. The construction documents will be generated next. Work is expected to be completed within the contracted timeframe.	Planning + Development	0	\$280,118
	Monrovia Hillside Wilderness Preserve	City of Monrovia	3204	The City of Monrovia has a Hillside Wilderness Preserve of over 800 acres. This project is to purchase additional parcels. The City staff has a list of identified properties based on location and connection value for incorporation into the Preserve.	The City of Monrovia has received a report from DGS supporting the appraisal of the first identified parcel and is moving forward in adding the 10 acres parcel to the preserve. This acquisition will leave the City funds to purchase more acreage in the Preserve.	Acquisition (+ Planning + Development)	20	\$810,000
	NASA Park	City of Downey	3419	The site is a former parking lot for the Boeing Company, Rockwell and other defense contractors at the former NASA site. The project includes trailhead and trailside facilities: restrooms, shade structure for educational purposes, benches, trashcans, drinking fountains and bike racks. The trail to be used by walkers and joggers will be enhanced with trees providing a canopy for shade, the creek like swale system and natural vegetation. The interpretive signage will provide information on the process being used to clean the storm water. The City plans to develop a combination low-impact/high impact recreation area with ball fields and a walking trail.	Landscaped architect was selected in June, 2005, and conceptual design approved at that time. Grantee has requested a meeting for mid May 2006, as many changes have occurred in the scope. Staff will meet with them to resolve. City still anticipates taking project to bid in June/July 2006	Planning + Development	0	\$250,000
	Native Habitat Docent Manual	Puente Hills Land-fill Native Habitat Preservation Authority	3602	The Native Habitat Docent Manual is a project that started out with the Habitat Fund and has been redirected to the Habitat Authority due to their capacity to complete the work at this time.	The Grant documents are in process of execution and the Habitat Authority has begun its work.	Interpretation	0	\$26,000



	Native Landscape Workshop	Rancho Santa Ana Botanic Garden	3585	To develop and a run a workshop for landscape architects, park planners, park maintenance, and others interested in native landscape.	Based on a action by the RMC board in May, 2006, two further workshops will be conducted in September, 2006.	Multiple Category	0	\$5,212
	Native Plant Garden Trail Restoration	Friends of the Seal Beach National Wildlife Refuge	3571	The project with the Friends of Seal Beach National Wildlife Refuge will restore their native plant walk trail on site. It will define and improve the trail in order to provide for easier access for handicapped visitors and the general public; achieve a more professional appearance, and provide for ease of future maintenance.	The grant agreement has been executed, the plans are complete. The Friends have asked to be released from their grant due to a timing issue. Staff is working with the Friends to ensure them that there is enough time to complete the work by Dec 2006.	Planning + Development	0	\$25,000
	Native Plant Palettes for the San Gabriel River	Rancho Santa Ana Botanic Garden	3422	This grant provides funding for development of a list of native plants that can be used as suitable vegetation palettes for establishment of native plants in the San Gabriel River Watershed.	The grantee has begun work on the project and is in the process of obtaining permits to collect samples of vegetation in the San Gabriel River Watershed. Work continues on the project.	Planning + Development	0	\$52,788




	Oak Canyon Nature Center	City of Anaheim	3425	The project proposes improvements to the interpretive trail and nature center entryway and outdoor amphitheatre. The nature center is a 58-acre natural park with a year-round stream, Walnut Creek, three adjoining canyons, and over four miles of hiking trails that traverse oak woodlands and coastal sage scrub.	The improvements to the Oak Canyon Nature Center are small but critical to implementing the Interpretive Plan for the park. The grantee has completed the installation and will be submitting payment request and final reports.	Planning + Development	0	\$6,050
	Olinda Historic Trail	City of Brea	3207	The project is to build a trail from the historic oil production area of the City of Brea up into the dedicated open space in the hillsides adjacent to Chino Hills State Park. The project will improve public access to open space, facilitate the growth of native plants and adapt existing oil company access roads for trail use.	The City has a contractor on board and is nearing completion of construction of the trail and its interpretive elements.	Planning + Development	0	\$98,050
	Olinda Historic Trail Phase II	City of Brea	3426	The Olinda Historic Trail II is the extension of the Olinda Trail funded by the RMC, allowing for the City to create a loop trail that takes advantage of the conservation easement.	. The City of Brea has completed the design and has a contractor in place. The early stages of trail construction are underway.	Planning + Development	0	\$45,000
	Organic Community Farm	Earth-Works Enterprises	3592	This grant is to fund several projects at the EarthWorks Community Organic Farm, located in South El Monte. A native plant revegetation meadow, a native plant demonstration garden, living visual screens, and development of related educational programs and materials are all proposed.	This grant is to fund several projects at the EarthWorks Community Organic Farm, located in South El Monte. A native plant revegetation meadow, a native plant demonstration garden, living visual screens, and development of related educational programs and materials are all proposed. The grant contract was signed in April and work is beginning.	Planning + Development	0	\$83,260
Project Management	Park Bond Project Management Services II (Capital Projects)	Mountains Recreation and Conservation Authority	3270	This grant provided for project management services over a two year period for the RMC workprogram.	Services provided under this grant included project management for RMC workprogram grants. Project Management services included development of project concepts with applicants, negotiations regarding the scope of work and budget, administration of grant agreement and close out of projects. All services have been completed.	Multiple Category	0	\$589,139


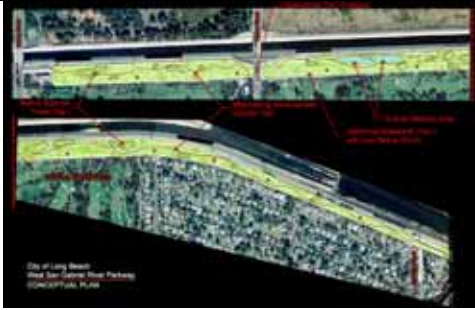

	Park Master Plan- Baldwin Park	City of Baldwin Park	3242	Development of a Master Plan to identify opportunities for increasing open space, including a plan for increasing the use of Walnut Creek Nature Park and creating access to Walnut Creek, a tributary of the San Gabriel River. MIG is the new planning consultant. The project is moving forward in the planning process, city and community outreach meetings are being held.	May 2006, City of Baldwin Park is working to clarify the scope of work to include RMC Objectives. A grant amendment and extension are pending	Planning	0	\$50,000
No Photo	Phase I Implementation of the Puente Creek Nature Education Center	City of La Puente	3594	Phase I of the Puente Creek Nature Education Center is designed to make the park functional while additional funding is being sought to complete the proposed project. The project elements included in Phase I are the walking trails, entrance gates and signage, irrigation, landscaping, decorative safety fence, wetland reproduction, interpretive displays, a temporary restroom, and parking spaces.	The RMC board approved a \$750,000 grant in May 2006.	Planning + Development	0	\$750,000
	Puente Creek Nature Education Center	City of La Puente	3224	The City of La Puente proposes acquisition of a vacant parcel along Puente Creek on which the Nature Center would be located. Situated between an existing school and the channelized creek, the sheltered education center will provide the local community as well as the students of the surrounding school districts the opportunity to gain knowledge of environmental issues that face our communities. The proposed facility will be an area which schools and other community organizations will be able to access for practical learning opportunities and passive recreation.	The City of La Puente has acquired a vacant parcel along Puente Creek to locate a Nature Center, which will provide local students and the community the opportunity to learn about current, relevant environmental issues. In May, 2006 the RMC Board approved a grant of \$750,000 to the city for construction of the Nature Center. Planning for this phase is underway.	Acquisition (+ Planning + Development)	0.95	\$400,000




	Ralph C. Dills Park Expansion	City of Paramount	3241	This is a grant to be used for the open space and passive use master planning process related to acreage acquired using Proposition A and 13 funds. These parcels are near the existing LA River park in Paramount. A grant amendment is pending for the project to move forward into the planning process.	During first quarter 2006, RMC staff met with Paramount to restart Master planning process regarding all parcels purchased with State funds. The City has prepared a request for qualifications in early May which will be released in Mid/late May.	Planning	0	\$200,000
	Rancho Los Alamitos Native Garden Restoration	Rancho Los Alamitos Foundation	3234	The project includes planting of natives, the construction of pathways, interpretive signage, and professional services related to design and planning for the native plantings and improved grading. Additional work will include restoration of a re-circulating water feature in the garden.	Installation of the water feature is now complete. The system is currently being tested to identify any remaining leaks. Once the grantee reports that testing is complete, this grant will be closed out.	Planning + Development	0	\$63,546
No Photo	Rio Dulce Acquisition	Mountains Recreation and Conservation Authority	3597	The grant will provide matching funds to MRCA to support a bid for acquisition of the Rio Dulce Ranch. The ranch, comprised of approximately 1,015 acres, is located south of State Route 14 (Antelope Valley Freeway), by Agua Dulce Canyon Road, north of the Santa Clara River, in the Soledad Canyon/Santa Clara River watershed.	The property was up for auction on May 26th, 2006 as a result of a bankruptcy filing by the owners. Bids received exceeded the appraised value of the property and MRCA was therefore not successful with their bid.	Acquisition (+ Planning + Development)	1015	Awaiting Proj Mgr action




	Rio Hondo - Roosevelt Avenue River Trail Entry	City of Montebello	3458	The City of Montebello's Roosevelt Avenue trailhead is the enhancement of a basic trailhead on the Rio Hondo bike path. This project will dovetail with a project that the City is working on with the Resources Agency to enhance the amenities along the Rio Hondo in Montebello.	The City has design plans that are 100%, the RMC staff has reviewed and commented on them. The City is in the process of the licensing with the County Flood Control District which looks to be complete. Construction will begin in the next quarter.	Planning + Development	0	\$200,000
No Photo	Rio Vista Nature Trail	City of El Monte and Amigos de los Rios	3465	This is the second phase following the Rio Vista Park rehabilitation. Funding would provide for landscaping and trail improvements to the Rio Hondo right of way from Rio Vista Park to Valley Boulevard connecting the park and the river trail. The improvements will include an entrance gate, native plants, benches and interpretive signage showcasing social and natural history.	The City of El Monte has approved a contract with Amigos de los Rios. Final design has been approved by the City Parks Commission and will be considered by City Council in June 2006.	Planning + Development	0	\$567,000
	Rio Vista Park Restoration and Conservation Project	City of El Monte	3221	The Rio Vista Park Restoration is a project that provides the restoration and rehabilitation of Rio Vista Park complete with interpretive displays, historical depictions of the Rio Hondo. Newly constructed bicycle trails and pedestrian walkways formed with native vegetation and historical growth will line the park and the Rio Hondo River and provide pedestrian connection points between major corridor of the City.	Demolition of the restoration areas is underway, the project has been supplemented with two grants from other agencies. Construction will begin in the next quarter with completion by Spring of 2007.	Planning + Development	0	\$375,200
<p>Wetland Recovery Project Mapping Needs (Sept 2004)</p> 	Riparian and Wetland Mapping	Southern California Coastal Water research Project	3557	The purpose of this project is to generate comprehensive up-to-date digital maps of: 1) wetland habitats (including estuaries, streams, lake wetlands, depressional wetlands and vernal pools), 2) riparian vegetation community composition, 3) riparian geomorphic boundary and 4) flood control infrastructure for the RMC Territory.	Recommendations on the scope of the project were made by the RMC Habitat and science Panel and have been transmitted to the grantee. SCCWRP and CSUN presented an overview of the wetland and riparian mapping project. SCCWRP staff has issued a subcontract with CSUN and work has commenced collecting the digital imagery to begin mapping. In addition, CSUN staff was trained by SFEL in techniques of riparian mapping.	Planning	0	\$104,000




	Rivers and Tributary Access Improvements	Watershed Conservation Authority	3248	<p>The WCA has identified trail access and signage improvements as a critical need for the river corridors in our territory. This grant has seven sub-grants that are for improvements and signage along the San Gabriel River and they are: Signage at Thienes Avenue, the Gateway to the Los Angeles River in Long Beach at Golden Shore, signage of the Lower Los Angeles River, access improvements at Arrow Highway in Irwindale, the Compton Creek Trail Project on the Los Angeles River, and signage of the San Gabriel River.</p>	<p>The seven sub-grants for improvements and signage along the San Gabriel River and they are: Signage at Thienes Avenue, the Gateway to the Los Angeles River in Long Beach at Golden Shore, signage of the Lower Los Angeles River, access improvements at Arrow Highway in Irwindale, the Compton Creek Trail Project on the Los Angeles River, and signage of the San Gabriel River.</p>	Planning + Development	0	\$500,000
<p>Grant Program Guide</p> 	RMC Grant Guidelines	Mountains Recreation and Conservation Authority	3272	<p>Services provided under this grant included development of grant guidelines and a workshop for successful grantees to provide assistance in selecting design and construction contractors.</p>	<p>The grant guidelines have been completed and updated. The consultant completed the workshops and provided all relevant material. An amendment to the scope of work also resulted in the production of GIS tools to help identify RMC projects.</p>	Multiple Category	0	\$148,422




	San Gabriel River Discovery Center	San Gabriel River Discovery Center Authority	3477	<p>The San Gabriel River Discovery Center (SGRDC) at the Whittier Narrows Nature Center (WNNC) includes planning and construction of a green/sustainable building (LEED Platinum level) which will serve multiple critical uses for the area. These uses include continued and expanded programs now in place at WNNC regarding the culture and natural area, serve as an introductory gateway to other resources in the watershed area, provide watershed awareness and conservation education, and also serve as a much needed meeting space for groups in the area. The site master planning includes restoration of the natural area for habitat, while providing outdoor educational experiences for all ages. Important trail nodal connections to trails in the Emerald Necklace are planned. A JPA consisting of LA County, Upper San Gabriel Valley Municipal Water District, Central Basin Water District and the RMC was formed in January 2006. The environmental review and fundraising processes will begin in Spring 2006, following completion of</p>	<p>The SGRDC approved the site concept design at its June 7, 2006 meeting. County Parks has initiated the environmental review process which is expected to last at least 18 months. Fundraising activities will also begin in earnest this summer.</p>	Planning + Development	0	\$3,000,000
	San Gabriel River Spreading Grounds	City of Pico Rivera	3228	<p>Development of a bike path/walking trail at the Spreading Grounds, landscaping, irrigation lines, the development of a rest area, lighting, interpretive signage and improved public entrances.</p>	<p>This project is being administered by LA County DPW. Work began in January (on the San Gabriel and Rio Hondo Spreading Grounds simultaneously) and is expected to be complete by September.</p>	Planning + Development	0	\$479,882
	San Gabriel River Trail Connector to Pio Pico State Historic Park	City of Whittier	3567	<p>Funds will allow for the development of construction drawings and final and complete construction of a new bike trail connecting the newly refurbished Pio Pico State Historic Park to the existing class one San Gabriel River Bikeway.</p>	<p>Grant funds will allow for the development of construction drawings and construction of a new bike trail, with possible trailhead, connecting the Pio Pico State Historic Park to the existing San Gabriel River Bikeway. The grant agreement was approved by the Whittier City Council in February. Consultant Kimley Horn is beginning work, and the steering committee kickoff meeting was held in April.</p>	Planning + Development	0	\$450,000




	San Gabriel River Trail Enhancement	City of Seal Beach	3239	The San Gabriel River Trail Enhancement project will create a plan and construction drawings to restore the existing San Gabriel River Trail and the trailside facilities from the Marina Dr. to Pacific Coast Highway and upgrade the site to feature new amenities.	The San Gabriel River Trail Enhancement is in the planning phase of the improvements to the City of Seal Beach terminus for the bike trail along the San Gabriel River. The City of Seal Beach has concept plans as well as construction documents that are at 100%. The CEQA Compliance process is at 88%, the cost estimates are at 77% and the City has left to complete the Community Workshops.	Planning	0	\$150,000
No Photo	San Gabriel River Trail Enhancement Development Project	City of Seal Beach	3573	The San Gabriel River Trail project is the development phase from the previous planning grant the City of Seal Beach received from RMC. The RMC approved this grant at the September 19, 2005 meeting that will pay for about half of the proposed improvements. The project will restore the existing San Gabriel River Trail and the trailside facilities from the First Street parking lot to Marina Drive and upgrade the site to feature new amenities. The restoration will include interpretive, way-finding and regulatory signage.	The City has 90% construction documents for the staging area at the end of the San Gabriel River. The City is moving through the permitting process with the Coastal Commission and is on track to begin construction in the Summer of 2006.	Planning + Development	0	\$500,000
	San Gabriel River Walk	City of Long Beach	3481	The San Gabriel River Walk is a project that takes an unused open space next to the western levee of the San Gabriel River and develops it into a passive park with pathways, and native landscaping.	At the first public meeting the City met with community concerns regarding the termination of the trail at the southerly end through a residential development. The City Staff has utilized this input from the community and did further research on alternative southerly access points. There will be another public meeting in this quarter to present these additional access alternatives and to select a preferred southerly access point to the trail.	Planning + Development	0	\$622,600
	San Gabriel River Watershed Habitat Restoration Assessment Project	San Gabriel Mountains Regional Conservancy	3247	The San Gabriel River Watershed Habitat Assessment project is a collection of research and data with an analysis in the Upper San Gabriel River, Walnut Creek and San Jose Creek sub watersheds.	The final report is complete and is currently being reviewed by staff. Review of the report will be on the agenda for the next RMC Science Panel's meeting and the final version will be posted to the website.	Planning	0	\$86,895

	San Jose Creek Bike Trail Planning	County of Los Angeles Department of Public Works	3230	Construction of 0.7 miles of a Class I bicycle trail with enhancements to landscape and hardscape. The project includes two bridges, one over San Jose Creek and another over the San Gabriel River. This project is part of a larger regional park plan to link cities as far east as Claremont to downtown Los Angeles.	This project is for the construction of 0.7 miles of a Class 1 bicycle trail, including two bridges (over San Jose Creek and the San Gabriel River). The trail is part of a larger regional park plan to link cities as far east as Claremont to downtown Los Angeles. An extension was approved, extending the performance period to July 31, 2006. Staff has been in contact with the DPW regarding the integration of this trail improvement the planning of the Duck Farm project.	Planning + Development	0	\$200,000
No Photo	Santa Fe Springs Park Improvements and Development of Nature Sanctuary	City of Santa Fe Springs	3595	Implementation of Phases I and II includes the functional elements of the park, such as the walking trails and landscaping. Decomposed granite walking trails, pedestrian bridges crossing the dry streambed, enhanced connections to the San Gabriel River bicycle trail, and native plantings will be installed. Succeeding phases will restore the streambed and create the picnic areas and sculptural elements of the Nature Exploration Zone.	The RMC board approved a \$600,000 grant in May 2006.	Planning + Development	0	Awaiting Proj Mgr action
	Santa Fe Springs Park Master Plan & Nature Sanctuary Feasibility Study	City of Santa Fe Springs	3210	This project will create a master plan for Santa Fe Springs Park and perform a feasibility study of the potential for creating a Nature Sanctuary on the 13 acre site adjacent and north of the Park, in between the 605 freeway and the San Gabriel River. The feasibility study will assess the feasibility of developing the 13-acre site as a Nature Sanctuary. In so doing, the study will contemplate the introduction and proliferation of native vegetation on the site, as well as consider the potential for interaction with the existing pedestrian/bike trail adjacent to the river.	This project is to develop a Master Plan for Santa Fe Springs Park and to assess the feasibility of expanding the park to create a Nature Park on the northern end. Grant was amended to extend performance period to June 30, 2006. The City is finalizing the plan/study, including mitigation requirements, and will be bringing the project to the RMC Board in May to request funding for implementation.	Planning	0	\$100,000
	Seal Beach Open Space Opportunities	City of Seal Beach	3244	This City of Seal Beach project is a small planning grant to investigate potential open space opportunities within the city. Various opportunities for planning, partnership, and property acquisition may already exist and the city wishes to develop a cohesive approach to maximize its efforts. Additionally, there are several small, fragmented efforts to restore parks and open space areas within the city, and this grant will allow for a master plan approach to future projects. The RMC funding funds a thorough investigation of open space opportunities, interested partners, property owner information, and significance to regional trails, recreational opportunities, as well as habitat value.	The City of Seal Beach has received the final report produced by RBF after their extensive survey of the City. The final report has been received, final payment requests are in process.	Planning	0	\$100,000

	Seventh Avenue Trailhead Improvements	Puente Hills Land-fill Native Habitat Preservation Authority	3262	Seventh Avenue Trailhead is a project working with the Habitat Authority in the northern Puente Hills creating a bioswale as well as access to the trails in the hills. The Seventh Avenue Trailhead improvements project involves the development of a trailhead, including interpretive signage, a parking area, ADA access, and vegetation, along with a bioswale.	The Habitat Authority has completed the project that included a trailhead, interpretive signage, a bioswale and connection to the Skyline Trail, they also hosted a trail opening event. RMC staff are awaiting the final report and payment request as the final tasks on this grant to be completed.	Planning + Development	0	\$231,739
	South Gate LA River Parkway Access Improvements	City of South Gate	3588	Improvements to the Southern Avenue and Hollydale Park Los Angeles River Parkway Access. Improvements will feature new gates, fencing, native landscaping and interpretative signage.	This project will provide access improvements to the Los Angeles River Parkway, at Southern Avenue and Hollydale Park. Improvements will feature new gates, fencing, native landscaping, and interpretive signage. The project manager is currently working with other City departments and LA Watershed Management District to finalize the design ideas, and create an RFP.	Planning + Development	0	\$250,000
	South Gate Riparian Habitat Restoration	North East Trees	3237	Land tenure negotiations are underway with various entities to allow the restoration of this acreage for riparian/open space uses. The property actually lies within the jurisdiction of the City of Lynwood.	As of May 2006 the RMC Board approved rescoping and extension of this project. Additional property is under consideration and the new scoping will allow feasibility assessment.	Planning + Development	0	\$500,000

	Sycamore Canyon Park Trail Development Project-Diamond Bar	City of Diamond Bar	3220	The Sycamore Canyon Trail Development project would develop the first trail increment of the City's five site city-wide trail system. Sycamore Canyon Park is an existing 50 acre city park that provides active recreation along with an undeveloped trail that begins at the existing parking lot near Golden Springs Drive and travels through undeveloped areas east toward Diamond Bar Boulevard. The undeveloped trails follow near an existing stream and four acres of walnut woodlands capable of supporting California Gnatcatcher and the Arroyo Toad. The proposal would result in a clearly defined path surfaced with decomposed granite and redwood headers.	This portion of the trail is complete. The trail opened on February 25, 2006.	Planning + Development	0	\$124,081
	Sycamore Canyon Trail Phase II	City of Diamond Bar	3582	Sycamore Canyon Trail II is a project that adds a length along the trail previously funded by the RMC. The Sycamore Park Trail travels .6 mile through Sycamore Canyon Park and another 1.5 miles in upper Sycamore Canyon all the way to the Diamond Bar Center. The project will create two improved access points and two class B trailheads.	The City will be releasing a request for bids for the project in the next quarter.	Planning + Development	0	\$140,000
	Tejon Park Expansion and Una Lake Equestrian Park	City of Palmdale	3227	Acquisition of Una Lake and surrounding properties to preserve habitat, restore wetlands, and use as passive open space parkland with additional parking as an expansion of Tejon Park. Project includes site design, entitlement and environmental review, site clearing, grading, installation of fencing, arena, arena soil, picnic areas, parking lot and infrastructure.	Since the grant was approved the property was sold to a developer. The Grantee has had early indications that development of the property will include a setaside of Una Lake for open space. The RMC approved an extension to the performance period based on the above scenario. No further progress has been reported since the previous report.	Acquisition (+ Planning + Development)	0	\$265,000
	Train Depot Staging Area	City of Bellflower	3291	Restoration of an existing historical train depot into a regional trail rest stop/staging area as well as transit facility. Rehabilitated train station will be used as a staging area and rest area for future bikeway trail (partial funding already obtained for this project). Conceptual plans have been completed and the City will submit preliminary plans to RMC staff in May/June 2006. The project is still on task to be completed no later than 12/31/06 within the constraints of the 18 month grant period.	Historical report and assessment of the train station has been completed. Concept design is complete construction drawings are at the 45% complete stage. Grantee has submitted request for grant extension to 12/31/06. Design plans begin ~ June '06. Grantee is aware and has agreed that all construction will be complete by 12/31/06 when the funds sunset (18 month grant).	Planning + Development	0	\$250,000

	Vincent Lugo Park Implementation Phase I	City of San Gabriel	3598	The grant will provide matching funds to the City for implementation of Phase 1 of the Vincent Lugo Park Masterplan. Phase 1 will include demolition of existing features; day-lighting of an existing drainage and installation of trails through a native landscape adjacent to the ball field.	Commencement of phase 1 will proceed based upon a grant of \$500,000 approved by the RMC Board in May, 2006 and confirmation of remaining funding sources.	Planning + Development	0	Awaiting Proj Mgr action
	Vincent Lugo Park Renovation	City of San Gabriel	3209	Develop a master plan for the renovation of Vincent Lugo Park. Master Plan will link San Gabriel Unified School District, the City, and Los Angeles County Flood Control District. Improvement contemplated include interpretive walking trail, reintroduction of native plants, picnic shelters reflecting the City's unique cultural heritage.	The City of San Gabriel has been working to prepare a Notice to Proceed for the design and preparation of construction documents for he Phase 1 implementation.	Planning	0	\$75,000
	Washington Park Implementation-Pasadena	City of Pasadena	3205	Development, including rehabilitation and restoration of portions of Washington Park. Includes an interpretive Center and historic El Molino Walkway, development of a demonstration garden, park arroyo and stage area and development of a historic picnic area.	Construction on the park improvements has begun. Demolition and preparation of the planting areas is complete.	Planning + Development	0	\$331,544
Project Management	Water Bond Project Management Services (Capital Projects)	Mountains Recreation and Conservation Authority	3591	At the direction of the San Gabriel and Lower Los Angeles Rivers and Mountains Conservancy (RMC) Executive Officer, the MRCA shall perform project management tasks for projects on the RMC Workprogram.	Services provided under this grant included project management for RMC workprogram grants. Project Management services included development of project concepts with applicants, negotiations regarding the scope of work and budget, administration of grant agreement and close out of projects.	Multiple Category	0	\$294,375

	Watershed Assessment and Planning Opportunities	Los Angeles and San Gabriel Rivers Watershed Council	3589	The RMC grant would provide support to the Watershed Council to prepare a concept proposal, the first step in a two-stage application process, to seek funds for (1) the establishment of a county-wide public official outreach and education program, and (2) utilize existing organizations (e.g., Councils of Government) to build a network of sub-watershed (or sub-regional) discussion groups focused on watershed issues, to improve stakeholder outreach on water management strategies, generate additional input on the articulation of regional priorities, and identify projects that will address these priorities.	The grantee shall develop a project proposal for Proposition 50, Ch. 7 grant programs, host a project workshop and coordinate regional interests in the program.	Multiple Category	0	\$9,240
	Watershed Education in Multi-lingual Communities	Regents of the University of California	3219	University of California Cooperative Education and East LA College are cooperating to develop a multilingual watershed interpretation and education curriculum to English as Second Language learners. Surveys with students using the program are in progress.	Grantee has implemented the curriculum with the East Los Angeles College ESL program. Revisions are in progress and survey for behavioral changes and learning are in progress.	Interpretation	0	\$32,094
	Watershed Education Outreach	TreePeople	3267	Treepeople will provide services including Agency and Policy Maker education, Environmental Learning Program and Public Affairs Consultation. Efforts continue to define this scope of work.	Grantee working with RMC staff to redefine scope of work, as planned scope is no longer feasible.	Planning	0	\$188,750
No Photo	Watershed Improvement Projects-LACC	Los Angeles Conservation Corps	3250	This grant to the Los Angeles Conservation Corps provides for improvements within the San Gabriel River Watershed such as invasive weed control, mulching and removal of debris. Working with the RMC staff, LACC will identify and develop a workplan for specific projects as needed.	Staff is working with LACC to identify further watershed improvement projects.	Planning + Development	0	\$150,000

